Tensegrity 2016 Project Timeline
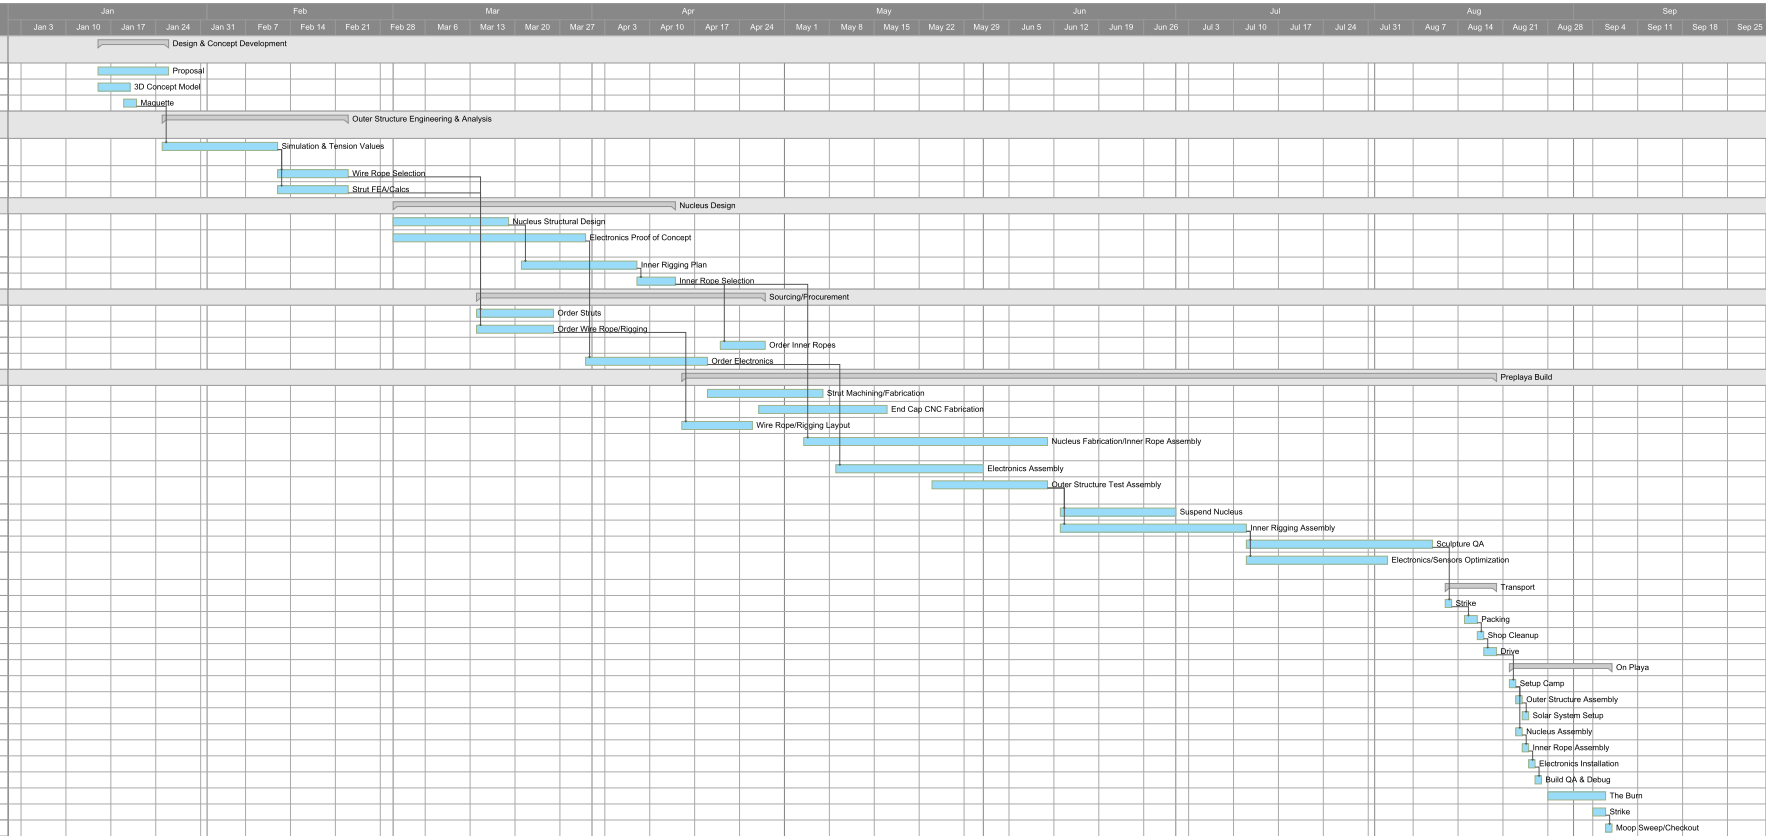
Task Name	Start Date	End Date
Design & Concept Development	01/15/16	01/25/16
Proposal	01/15/16	01/25/16
3D Concept Model	01/15/16	01/19/16
Maquette	01/19/16	01/20/16
Outer Structure Engineering & Analysis	01/25/16	02/22/16
Simulation & Tension Values	01/25/16	02/11/16
Wire Rope Selection	02/12/16	02/22/16
Strut FEA/Calcs	02/12/16	02/22/16
Nucleus Design	03/01/16	04/13/16
Nucleus Structural Design	03/01/16	03/18/16
Electronics Proof of Concept	03/01/16	03/30/16
Inner Rigging Plan	03/21/16	04/07/16
Inner Rope Selection	04/08/16	04/13/16
Sourcing/Procurement	03/14/16	04/27/16
Order Struts	03/14/16	03/25/16
Order Wire Rope/Rigging	03/14/16	03/25/16
Order Inner Ropes	04/21/16	04/27/16
Order Electronics	03/31/16	04/18/16
Preplaya Build	04/15/16	08/19/16
Strut Machining/Fabrication	04/19/16	05/06/16
End Cap CNC Fabrication	04/27/16	05/16/16
Wire Rope/Rigging Layout	04/15/16	04/25/16
Nucleus Fabrication/Inner Rope Assembly	05/04/16	06/10/16
Electronics Assembly	05/09/16	05/31/16
Outer Structure Test Assembly	05/24/16	06/10/16
Suspend Nucleus	06/13/16	06/30/16
Inner Rigging Assembly	06/13/16	07/11/16
Sculpture QA	07/12/16	08/09/16
Electronics/Sensors Optimization	07/12/16	08/02/16
Transport	08/12/16	08/19/16
Strike	08/12/16	08/12/16
Packing	08/15/16	08/16/16
Shop Cleanup	08/17/16	08/17/16
Drive	08/18/16	08/19/16
On Playa	08/22/16	09/06/16
Setup Camp	08/22/16	08/22/16
Outer Structure Assembly	08/23/16	08/23/16
Solar System Setup	08/24/16	08/24/16
Nucleus Assembly	08/23/16	08/23/16
Inner Rope Assembly	08/24/16	08/24/16
Electronics Installation	08/25/16	08/25/16
Build QA & Debug	08/26/16	08/26/16
The Burn	08/28/16	09/05/16
Strike	09/04/16	09/05/16
Moop Sweep/Checkout	09/06/16	09/06/16
